


A construction project for resurfacing and drainage improvements on Northern Spring Gulch Road, County Road 22-4, between Riva Ridge Road and Bar BC Road. This includes paving of the existing gravel road, approximately 1 mile in length and replacement of, and installation of new drainage and irrigation culverts.

Staff has worked on this project for several years to attempt to acquire additional road easement to allow for traffic calming elements, more space for a pathway, and irrigation ditch alterations. Unfortunately, this has not been successful to date. Staff intends to continue to plan for a separated pathway on the west side of the road, but not as part of this project.

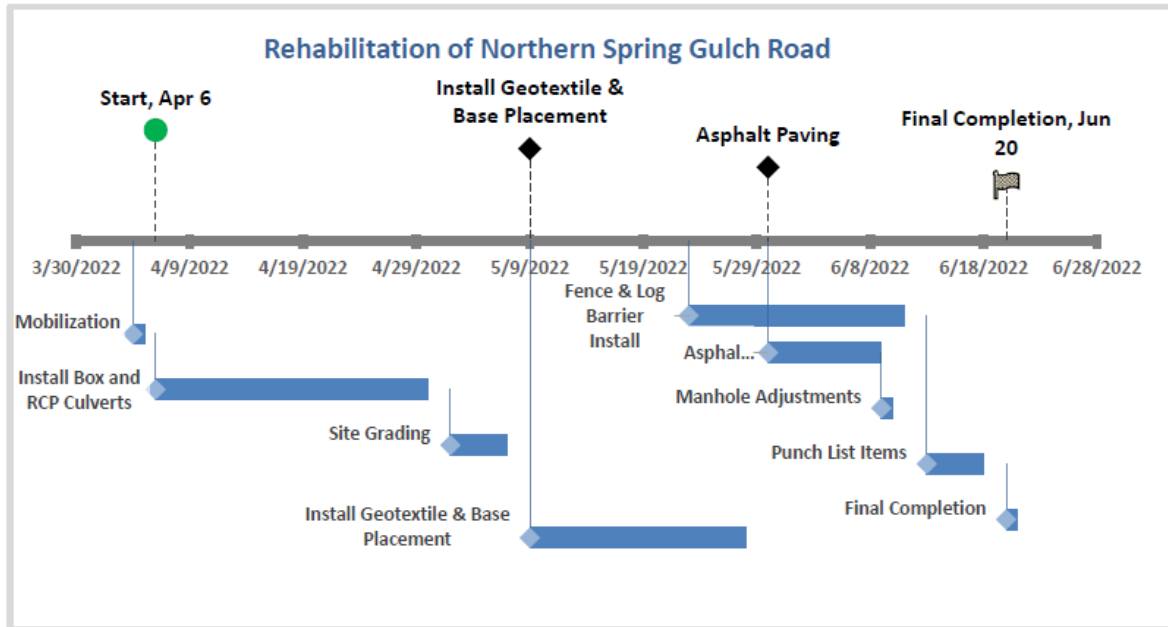


Tasks

Start	End	Duration	Label
4/4/2022	4/5/2022	1	Mobilization
4/6/2022	4/29/2022	24	Install Box and RCP Culverts
5/2/2022	5/6/2022	5	Site Grading
5/9/2022	5/27/2022	19	Install Geotextile & Base Placement
5/30/2022	6/8/2022	10	Asphalt Paving
6/9/2022	6/9/2022	1	Manhole Adjustments
5/23/2022	6/10/2022	19	Fence & Log Barrier Install
6/13/2022	6/17/2022	5	Punch List Items
6/20/2022	6/20/2022	1	Final Completion



END OF PROJECT  
(END OF PAVEMENT)

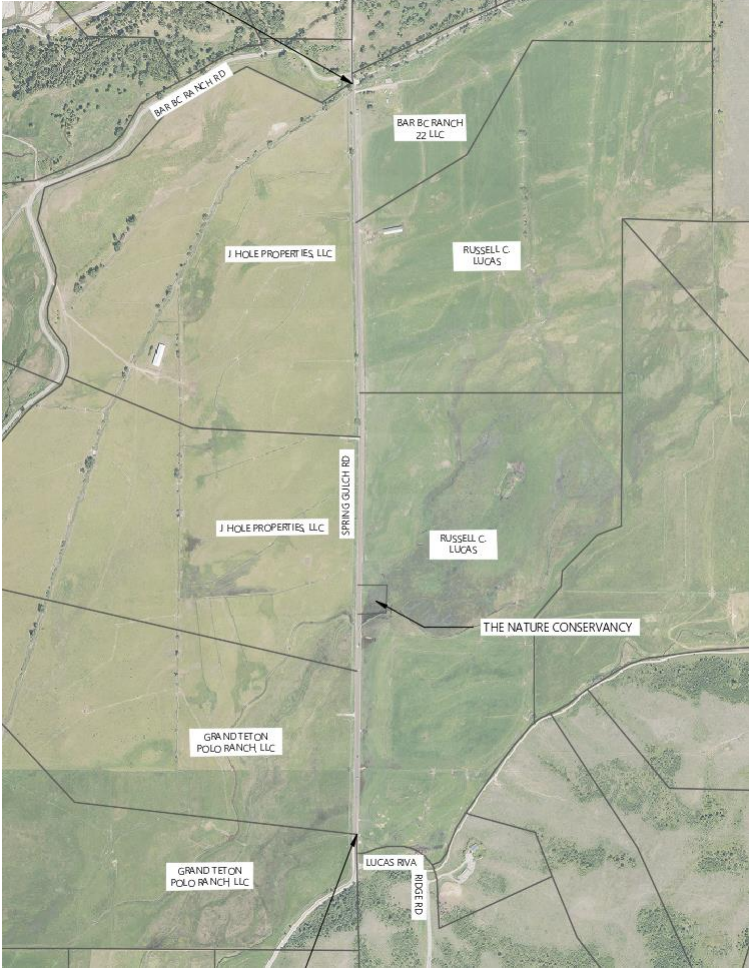

START OF PROJECT  
(END OF PAVEMENT)

